Crosslines Community Facility

Phases

Phase	Planned Finish
Project Execution	Spring 2016
Project Closeout	Summer 2016


Project Description
This project consists of the renovation of an approximately 10,000 sf facility to assist with the increased demand of services provided since the tornado. Their new facility is located at 320 S. School Avenue.

Vendors

Vendor	Contact	Phone
Arkbild	Chris Sams	816-806-7758
Crosslines	Kathy Lewis	417-782-8384



Funding

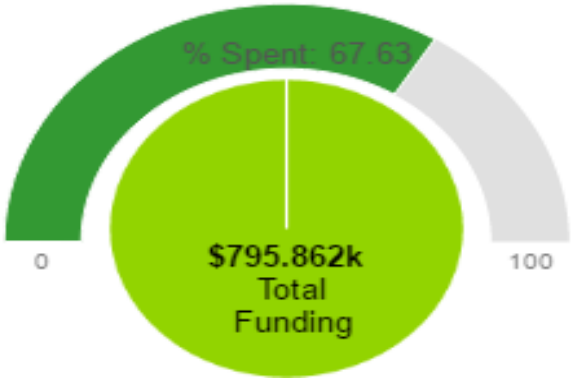

Funding($):
$795,862.000
CDBG

Expended($):
$538,261.390
