CITY

OF

JOPLIN, MISSOURI

BID PACKAGE

#2017-12

for

PRE-ENGINEERED PARK SHELTER

JOPLIN PARKS DEPARTMENT
3301 W. FIRST STREET
JOPLIN, MO 64801

(417) 625 4750

NOTICE TO BIDDERS

The City of Joplin, Missouri will accept sealed bid proposals until 2:00 P.M., Thursday, May 25th, 2017 at the Joplin Parks Department located at 3301 W. First Street, Joplin, Missouri, 64801 to PURCHASE the following:

PRE-ENGINEERED PARKS SHELTER

Specifications and bid forms are available from Steve Curry, Parks Dept., by calling 417-625 4750 or by writing to the address indicated above. Any bids received after the specified deadline will be returned to the vendor.

The City reserves the right to evaluate all bids, to reject any or all bids and re-bid at a later date. The City may waive any irregularities in the bid or negotiate variances from specifications, and make awards that are in the best interests of the City. The City will have final decision in all matters regarding acceptance of bids and issuance of awards.

The City encourages minority and female owned businesses to submit bids on all City purchases.

Leslie Haase, CPA
Finance Director

Publication Date: Wednesday, April 26th, 2017

INSTRUCTIONS TO BIDDERS

The City of Joplin, Missouri proposes to PURCHASE the following:

Pre-Engineered Parks Shelter

All bids shall have firm-fixed F.O.B. Joplin; Missouri price and shall be honored for a minimum of ninety (90) days following the bid opening.

All bids shall be exclusive of Federal, State, and City taxes.

It is the intent of the specifications included with this bid document to generally describe the item(s) desired in sufficient detail as to secure bids on comparable items. All parts not specifically mentioned which are necessary in order for the item(s) to perform as intended shall be included. The strength, quality of workmanship, and material shall be in accordance with the best trade practices.

Specification variances, manufacturer's literature and additional information should be attached to the bid form. All blanks on the attached bid specifications shall be filled in completely and accurately. Any bid not meeting this requirement may be considered non-responsive.

Any protest or grievance must be issued in writing and delivered to the office of the Director of Finance within ten (10) days following the bid opening. Any protest filed after this time period has elapsed will not be considered.

The City encourages selection of products manufactured, assembled and/or produced in the United States, as long as the quality and price are comparable with other items bid.

Businesses which are located within the city limits of Joplin may be given preference in the awarding of a bid, providing the bid from the local business does not exceed the lowest bid by more than 3% or $2,500, whichever is less.

The City may give preference to vendors handling products that contain post-consumer recovered materials, providing the bid does not exceed the lowest bid by more than 5% or $2,500, whichever is less.

Once the bids are reviewed and evaluated, the successful vendor will be notified, in writing, and will receive an authorized City of Joplin purchase order. Verbal acknowledgments will not be considered as official notification and will not obligate the City in any way. Delivery or performance should not be completed without the receipt of an authorized purchase order.

Minimum information to be submitted with each bid shall consist of the following:

1. Verification of Bid Specifications (with variances noted)
2. Bid Form

MARK BID ENVELOPES: "#2017-12 Pre-Engineered Park Shelter, Thursday, May 25th, 2017."

Questions concerning the specifications and bidding procedures should be directed to Steve Curry, Parks Dept., 3301 W. First St, Joplin, MO, 64801 or by phoning 417-625-4750.

Notice to Contractors
Bid Specifications for Pre-Engineered Parks Shelter

1. **Scope** -

To provide one, pre-cut, pre-drilled, professionally designed, Park shelter kit that requires minimal on site fabrication. **Successful bidder shall provide 3**

sets of building plans after receipt of a purchase order from the City of Joplin. Design must be approved and stamped by a structural engineer registered in the State of Missouri and must include footing and pier drawings . Structure shall be powder coated steel frame with commercial grade 24 ga. raised-rib steel roof.

2. **Design-**

Building shall be designed to meet 2015 IBC 115 MPH winds and 30 lb roof snow load, non-reduced. After receipt of a purchase order the manufacturer shall furnish erection drawings showing details for construction and footing and pier detail.

Note: See attached sheet for building dimensions.

3. **Specifications** -

A. Roof Dimensions, point to point 45'-0"
Column Dimensions (center to center) 40'-0"
Eave Height 8'-0"
Roof Height @ Peak ±15'-11 ¾"
Main Hip Roof 4:12 pitch
Square Feet Under Roof ±810
Columns shall be 10"x 10" steel tube, .188" minimum wall thickness.
All beams shall be structural steel tube sized according to engineering.
Rafter beams shall be one piece construction with mitered welded corners.
All bolts shall be A-325 or A-307 and hidden at all connections.
Roofing shall be 24 gauge R-Panel steel pre-cut and pre-finished with ribs running with the slope
of the roof.
Trim shall be 24 gauge pre-finished to match roofing.
Open or welded "C" channels, "I" beams, "S" or "Z" purlins or angle iron shall not be allowed.
Column surrounds by others.

B. All welding shall be done in accordance with the latest AWS standards and all welds are to develop full strength of component parts.

All fabricated steel and structural components shall be shot blasted steel with factory applied zinc rich primer and TGIC Polyester powder coating (5-6 mil. min. thickness on exterior and 3 mil. min on interior).

C. Roof metal- 24 ga. - 80,000 psi high tensile strength. 30 year warranty on rib-metal finish. (owner will select color)

D. Hardware- All hardware shall be zinc-plated. All required fasteners and bolts shall be included (excluding anchor bolts).

E. All eave and rake trim included.

4. **Miscellaneous-**

Concrete slab, footings, site preparation and installation shall be the owners responsibility.

5. Delivery-

All shipping costs shall be included in bid price and delivery shall be within 12 weeks of receipt of a Purchase Order number.

Delivery location is Ewert Park located at 7th and Illinois Street in Joplin Mo.

Contact Person: Steve Curry
Joplin Parks and Recreation
3301 West First Street
Joplin Mo. 64801
417-625 4750

CITY OF JOPLIN
BID FORM

DESCRIPTION: PRE-ENGINEERED PARK SHELTER

BASE BID DELIVERED: 45’ HALF HEXAGON _____

F.O.B. JOPLIN, MISSOURI

DELIVERY AFTER RECEIPT OF ORDER: 12 weeks

COMPANY: _____

ADDRESS: _____

_____

_____

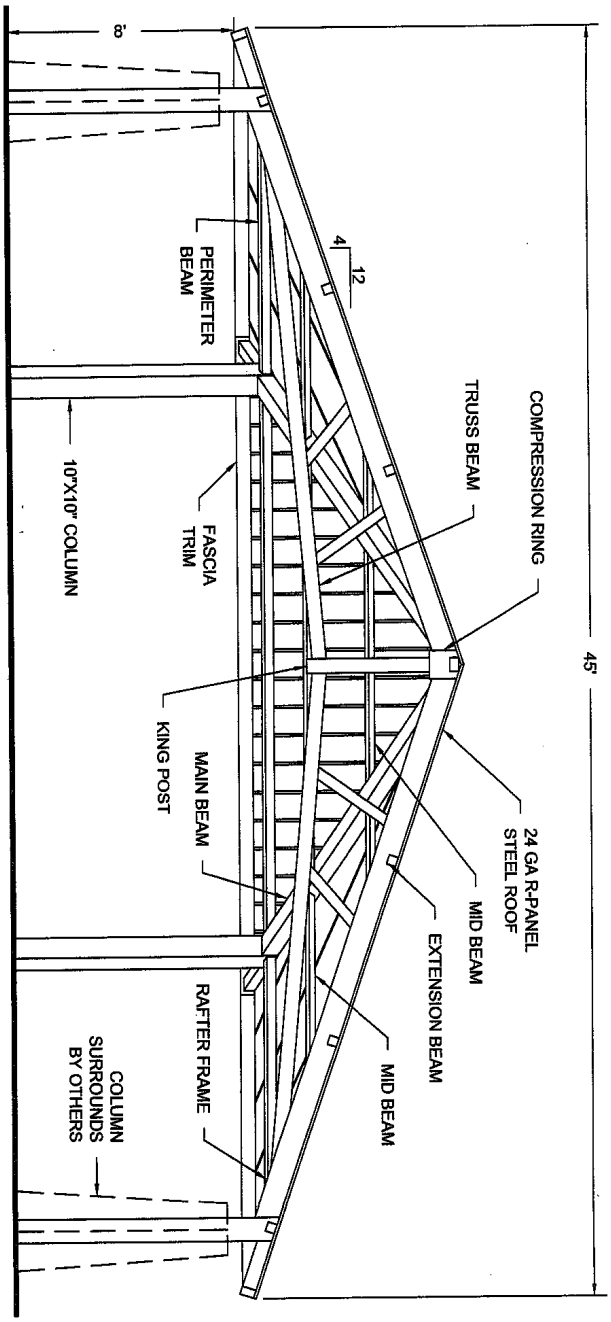
TELEPHONE:_____

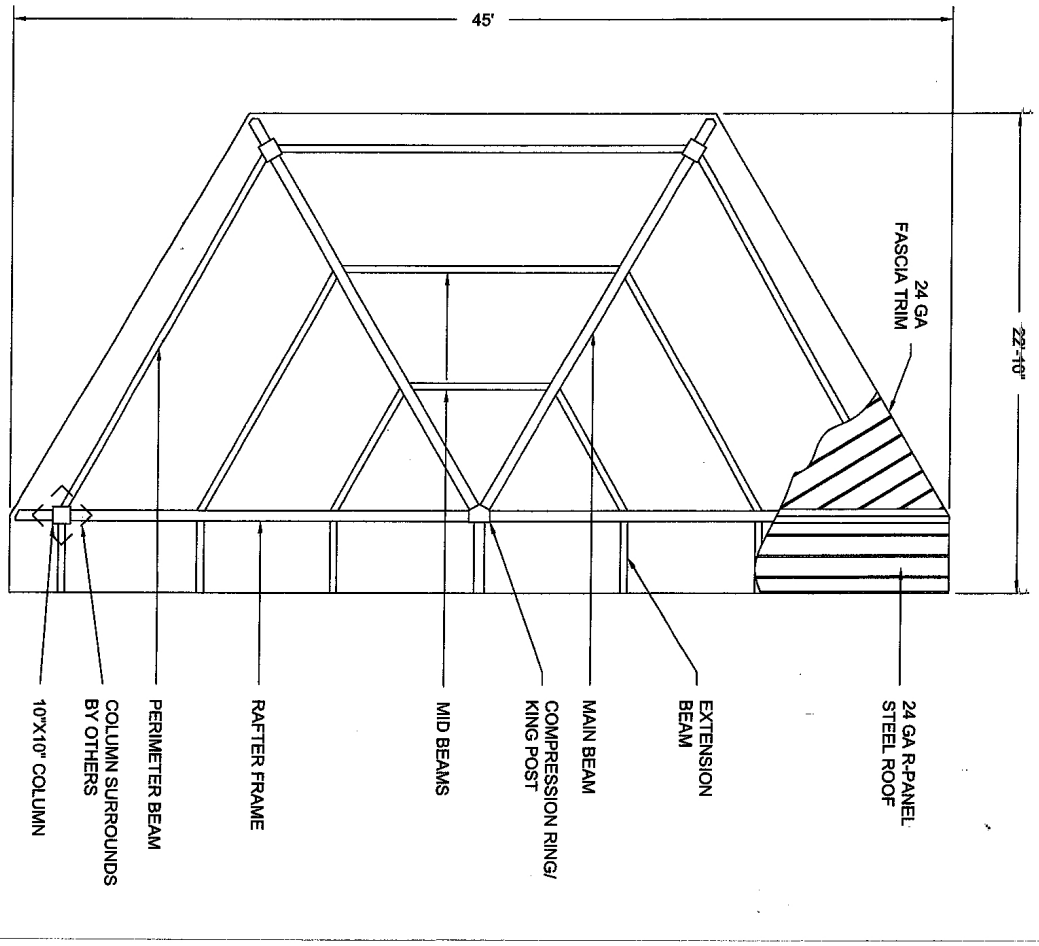
SIGNATURE:_____

_____

MINORITY: _____FEMALE:_____

MARK BID ENVELOPES : ***“#2017-12, Pre-Engineered Park Shelter , Thursday, May, 25th 2017”***


8'
45'
4
12
PERIMETER BEAM
10"X10" COLUMN
FASCIA TRIM
KING POST
MAIN BEAM
RAFTER FRAME
COLUMN SURROUNDS BY OTHERS
TRUSS BEAM
COMPRESSION RING
24 GA R-PANEL STEEL ROOF
MID BEAM
EXTENSION BEAM
MID BEAM


45'
22'-10"
24 GA
FASCIA TRIM
24 GA R-PANEL
STEEL ROOF
EXTENSION
BEAM
MAIN BEAM
COMPRESSION RING/
KING POST
MID BEAMS
RAFTER FRAME
PERIMETER BEAM
COLUMN SURROUNDS
BY OTHERS
10"X10" COLUMN
